

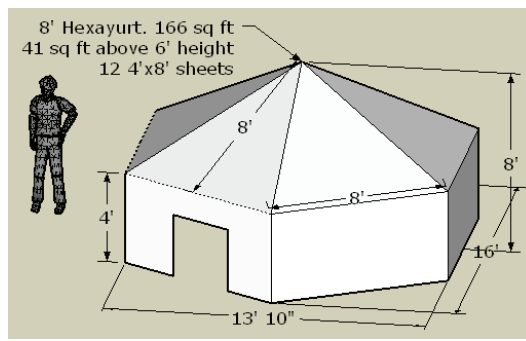


Specifications:

- 8' Hexayurt
- 166 square feet
- 12 sheets of 4' x 8' rigid insulation, at least 1" thick
- 315 feet of 3" tape
- 370 feet of 6" tape
- 2 people for 95% of the work
- Ships in 4' x 8' stack




Cut Panels:

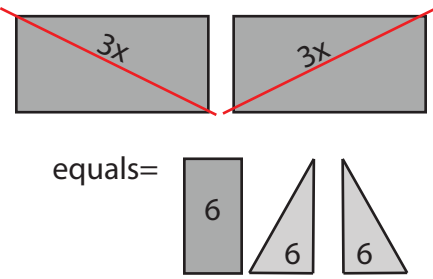


Taping plan: before making hinges, seal these raw edges of all panels with 3" wide tape (8' side of rectangles, 2' side and 'points' of triangles). You will have 6 edges to seal after making hinges.



Connect 3 panels, with a tight hinge and a loose hinge to make a "half-wall." The loose hinge for walls has a gap equal to the thickness of your panel. Note which side of the panels the tape goes on in the "first step" or "inseam" of each hinge, this puts the logos on the inside of the yurt.

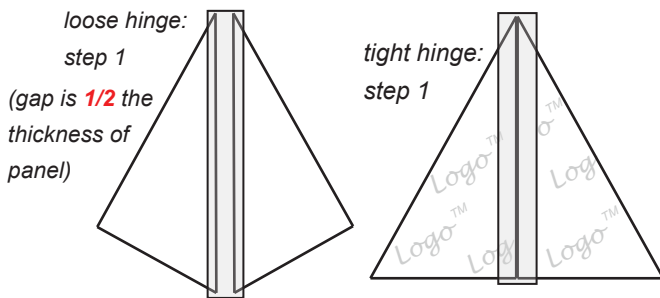

The roof hinges are more difficult. Start with the loose hinge--the gap is 1/2 the thickness of the panel (using 1" panels, gap=1/2". If 2" panels, 1" gap, etc). Step 1 of the roof loose hinge is on the non-logo side of the panels. Repeat this hinge 6 times. The tight hinge is the same as for the walls. Repeat 4 times. You now have 2 roof halves.

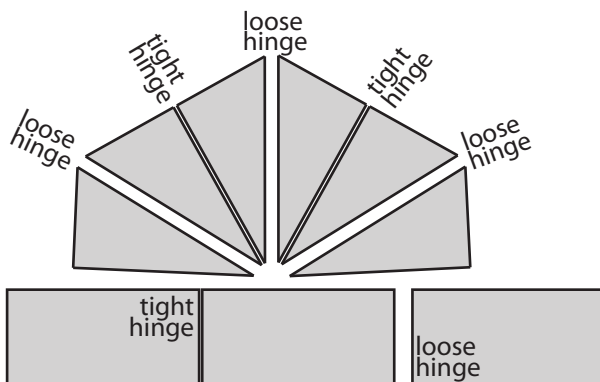

Finished product:
2 roof halves,
2 wall-halves.
Ships 4' x 8'

