ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	Section 1	3 days	Thu 2/14/13	Mon 2/18/13		Jeanne
2	Section 2	10 days	Tue 2/19/13	Mon 3/4/13	1	Reina
3	Client Meeting #1	1 day	Fri 2/22/13	Fri 2/22/13		Vlad
4	Lit Review	7 days	Tue 2/19/13	Wed 2/27/13	2SS	Reina
5	Client Meeting #2	1 day	Fri 3/1/13	Fri 3/1/13	4	Jeanne
6	Problem Analysis	2 days	Fri 3/1/13	Mon 3/4/13	5SS	Vlad
7	Research material ideas	5 days	Mon 3/4/13	Fri 3/8/13		Jeanne
8	Client Meeting #3	1 day	Fri 3/8/13	Fri 3/8/13		Vlad
9	Section 3	7 days	Tue 3/5/13	Wed 3/13/13		Reina
10	Client Meeting #4	1 day	Fri 3/15/13	Fri 3/15/13		Jeanne
11	Section 4	8 days	Thu 3/14/13	Mon 3/25/13	9	Vlad
12	Client Meeting #5	1 day	Fri 3/29/13	Fri 3/29/13		Jeanne
13	Client Meeting #6	1 day	Fri 4/5/13	Fri 4/5/13		Vlad
14	Section 5	18 days	Thu 3/14/13	Mon 4/8/13	11SS	Reina

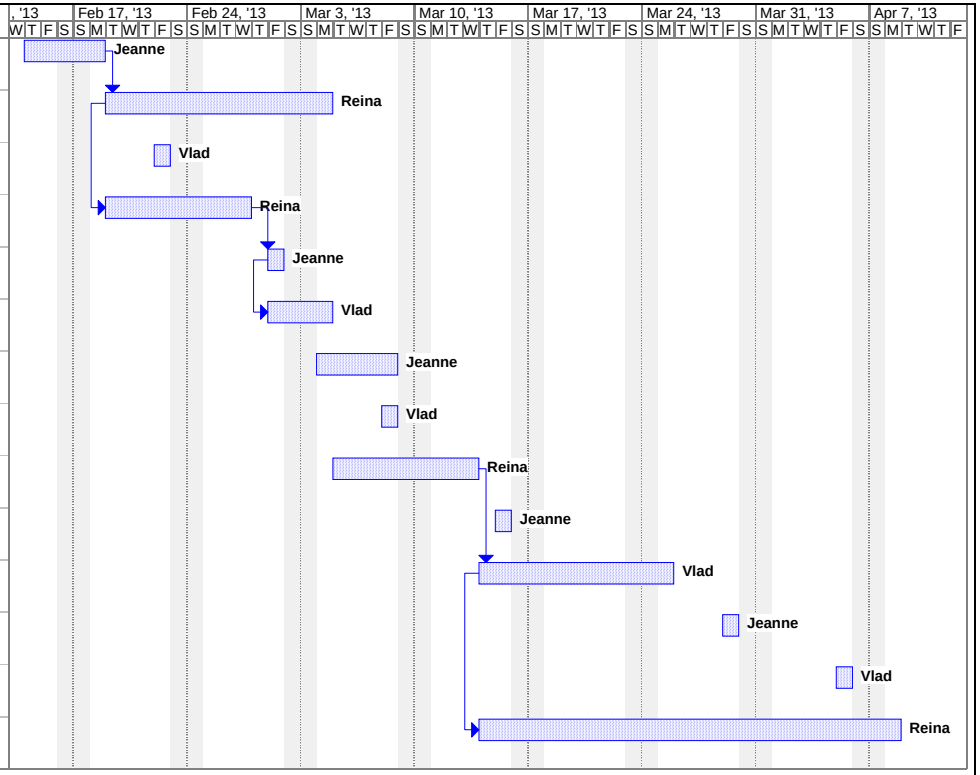

Project: Gantt Chart2.mpp
Date: Thu 5/9/13

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
